

COUNCIL PRIORITY 5: Belleview Corridor

MON 5/22/17 - FRI 8/10/18

% COMPLETE

95%




MILESTONES

All project milestones.

Name	Finish
Community Meeting (Open House)	Thu 3/22/18
Planning Commission Study Session: Final Plan	Mon 5/14/18
Study Session Meeting: Council to review final plan	Tue 5/22/18
Planning Commission: Hearing	Mon 6/11/18
Council Meeting: Resolution to Adopt Plan	Tue 7/17/18

% COMPLETE

Status for all top-level tasks.

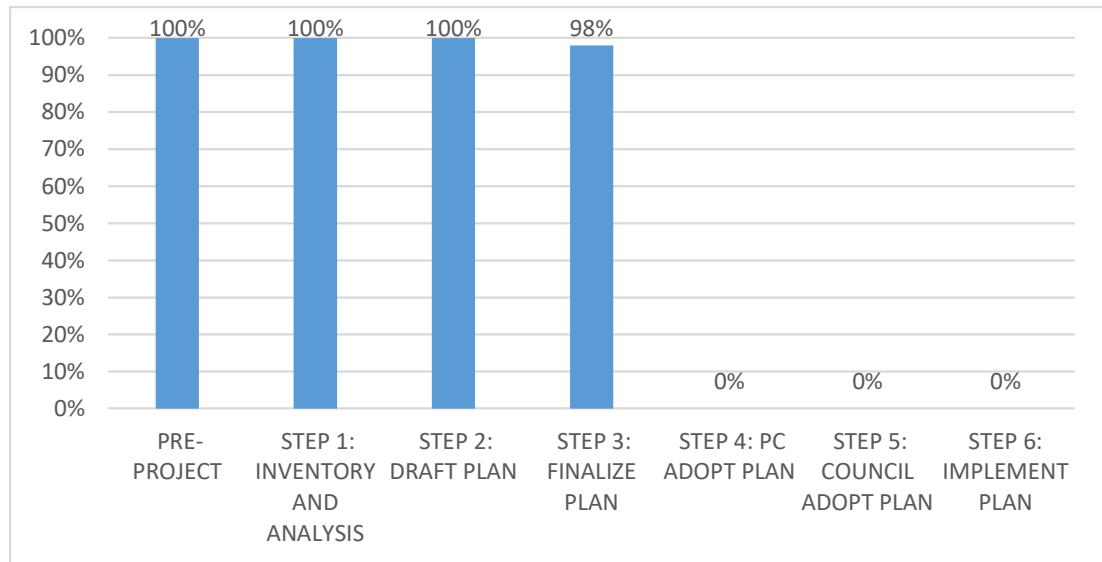

Summary

Status and timing of major project steps.

Name	Start	Finish	Duration	% Complete
PRE-PROJECT	Mon 5/22/17	Tue 8/22/17	66 days	100%
STEP 1: INVENTORY AND ANALYSIS	Mon 10/2/17	Fri 12/29/17	65 days	100%
STEP 2: DRAFT PLAN	Mon 1/1/18	Wed 2/28/18	43 days	100%
STEP 3: FINALIZE PLAN	Wed 3/28/18	Tue 5/22/18	40 days	98%
STEP 4: PC ADOPT PLAN	Mon 6/11/18	Mon 6/11/18	0 days	0%
STEP 5: COUNCIL ADOPT PLAN	Tue 7/17/18	Tue 7/17/18	1 day	0%
STEP 6: IMPLEMENT PLAN	Wed 7/18/18	Fri 8/10/18	18 days	0%
